


Description: Norman Wells CCG Wharf Repairs, Dredging
Project Number: 084190.001
Contract Number: EP922-1821221/001/PWU

Dredging Plan:

Originating at the upstream north border of the identified dredging area
Slots approx. 5m in width will extend from North to South of the dredging perimeter
Material will be excavated to specified depth as per supplied drawings (North to South)
Once first slot is excavated, the same procedure will be followed after moving downstream approx 5m
Estimated total of (26x) 5m slots will be utilized to complete the dredging

Dredging Outline

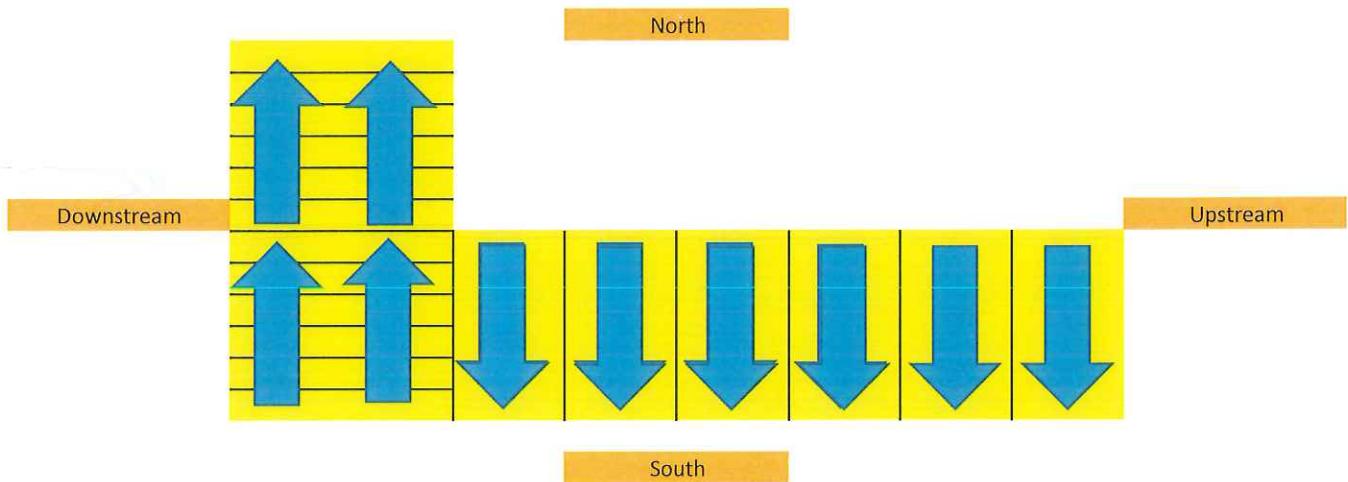

**not to scale
