MGM ENERGY CORP.

Report No 10

WELL DIAGRAM EXISTING

ALL DEPTHS ARE mKB

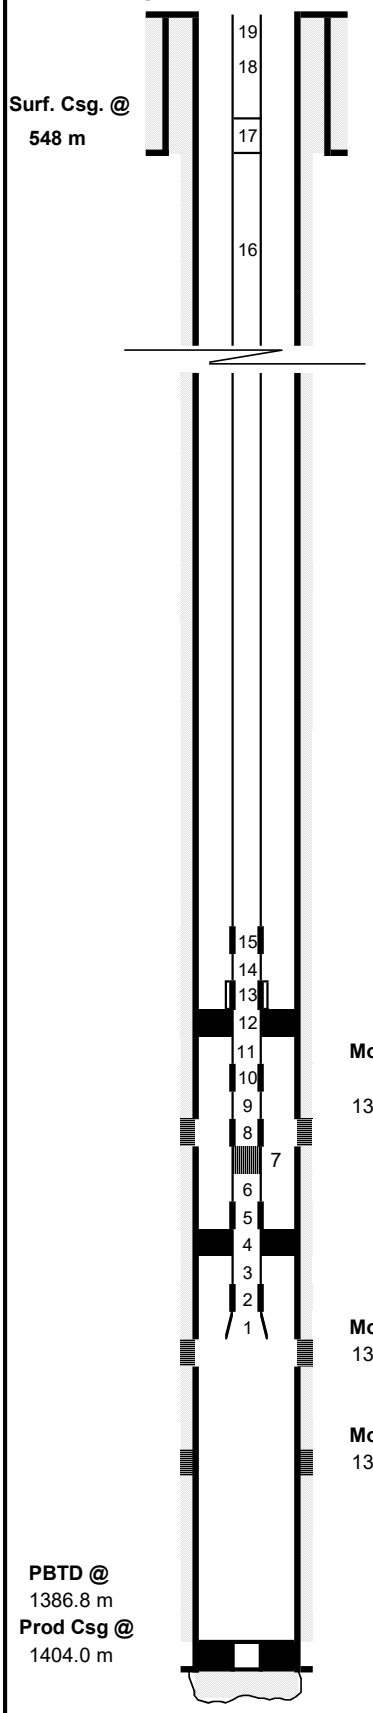

WELL NAME: MGG WEST NOGHA K-14

PREPARED BY: Mike Periard/Barry Beitz				DATE:	2004-05-14
ELEVATIONS (meters):				Licence No:	WID 2006
TD	1,404.20	KB Elev.	313.20	KB to CF Dist. H	4.70
PBTD	1,386.80	Ground Elev.	308.00	KB to Ground	5.20

CASING/TUBING	SIZE (mm)	WEIGHT (Kg/m)	GRADE	DEPTHS (m)	
Surface Casing	244.50	53.50	J-55	548.00	37 jts.
			LT&C		
Production Casing	177.80	43.16	L-80	1,404.00	113 jts.
			LT&C		
Prod Liner	N/A				
Tubing	73.00	9.67	L-80	1,369.42	140 Jts
			EUE		

BOTTOM HOLE ASSEMBLY:

ITEM	DESCRIPTION	LENGTH (m)	Top at (m KB)
1	1 - 73 mm Re-entry guide	0.15	1,369.27
2	1 - 73 mm x 55.58 mm **"RN"** nipple c/w 51.05 mm No-Go	0.50	1,368.77
3	1 - 73 mm EUE 9.67 kg/m L-80 pup joint	1.25	1,367.52
4	177.8 mm Halliburton G-777 hydraulic set packer 11 daNs shear	1.68	1,365.84
5	1 - 73 mm x 55.58 mm **"R"** nipple	0.48	1,365.36
6	1 - 73 mm EUE 9.67 kg/m L-80 pup joint	0.64	1,364.72
7	1 - 73 mm Halliburton XA sliding sleeve c/w 58.75 mm **X** profile **closed**	1.12	1,363.60
8	1 - 73 mm blast joint	2.99	1,360.61
9	1 - 73 mm EUE 9.67 kg/m L-80 pup joint	2.47	1,358.14
10	1 - 73 mm x 58.75 mm **X** nipple	0.37	1,357.77
11	1 - 73 mm EUE 9.67 kg/m L-80 pup joint	2.47	1,355.30
12	177.8 mm Halliburton G-777 hydraulic set packer 11 daNs shear	1.68	1,353.62
13	177.8 mm Halliburton HD On/Off assembly c/w 58.75 mm **X** profile	0.67	1,352.95
14	1 - 73 mm EUE 9.67 kg/m L-80 pup joint	3.08	1,349.87
15	1 - 73 mm x 58.75 mm **X** nipple **plug in place**	0.37	1,349.50
16	139- 73mm, 9.67 kg/m, L-80 joints	1,332.19	17.31
17	2- 73mm, 9.67 kg/m, L-80 pup joint (1 x 0.20 m / 1 x 2.47 m)	2.67	14.64
18	1- 73mm, 9.67 kg/m, L-80 joint	9.53	5.11
	Compression of 5000 daN	-0.32	5.43
	Log Correction	1.02	4.41
19	179.4 mm x 73 mm Cameron extended neck chemical line prep tbg. Hngr	0.26	4.15
	June 16, 2016 Installed Cameron 1 way back pressure valve in Tubing Hangar		4.15
			4.15
			4.15
			4.15
			4.15
	NOTE: A-3 plug set @ 21 mcf		4.15
			4.15
			4.15
			4.15
	TALLY	1,365.27	
	KB TO TUBING HEAD	4.15	
	TUBING BOTTOM	1,369.42	

PERFORATION INTERVALS

1360.8 - 1363.2 mkb - Mount Clark "A"
1369.7 - 1372.5 mkb - Mount Clark "B"
1375.0 - 1379.0 mkb - Mount Clark "C"

NOTE:

Cement top @ 450 mKB.
